#2019.2020.02 Chardon-Bershire (WWTP) - TRAX Construction Company

Preliminary
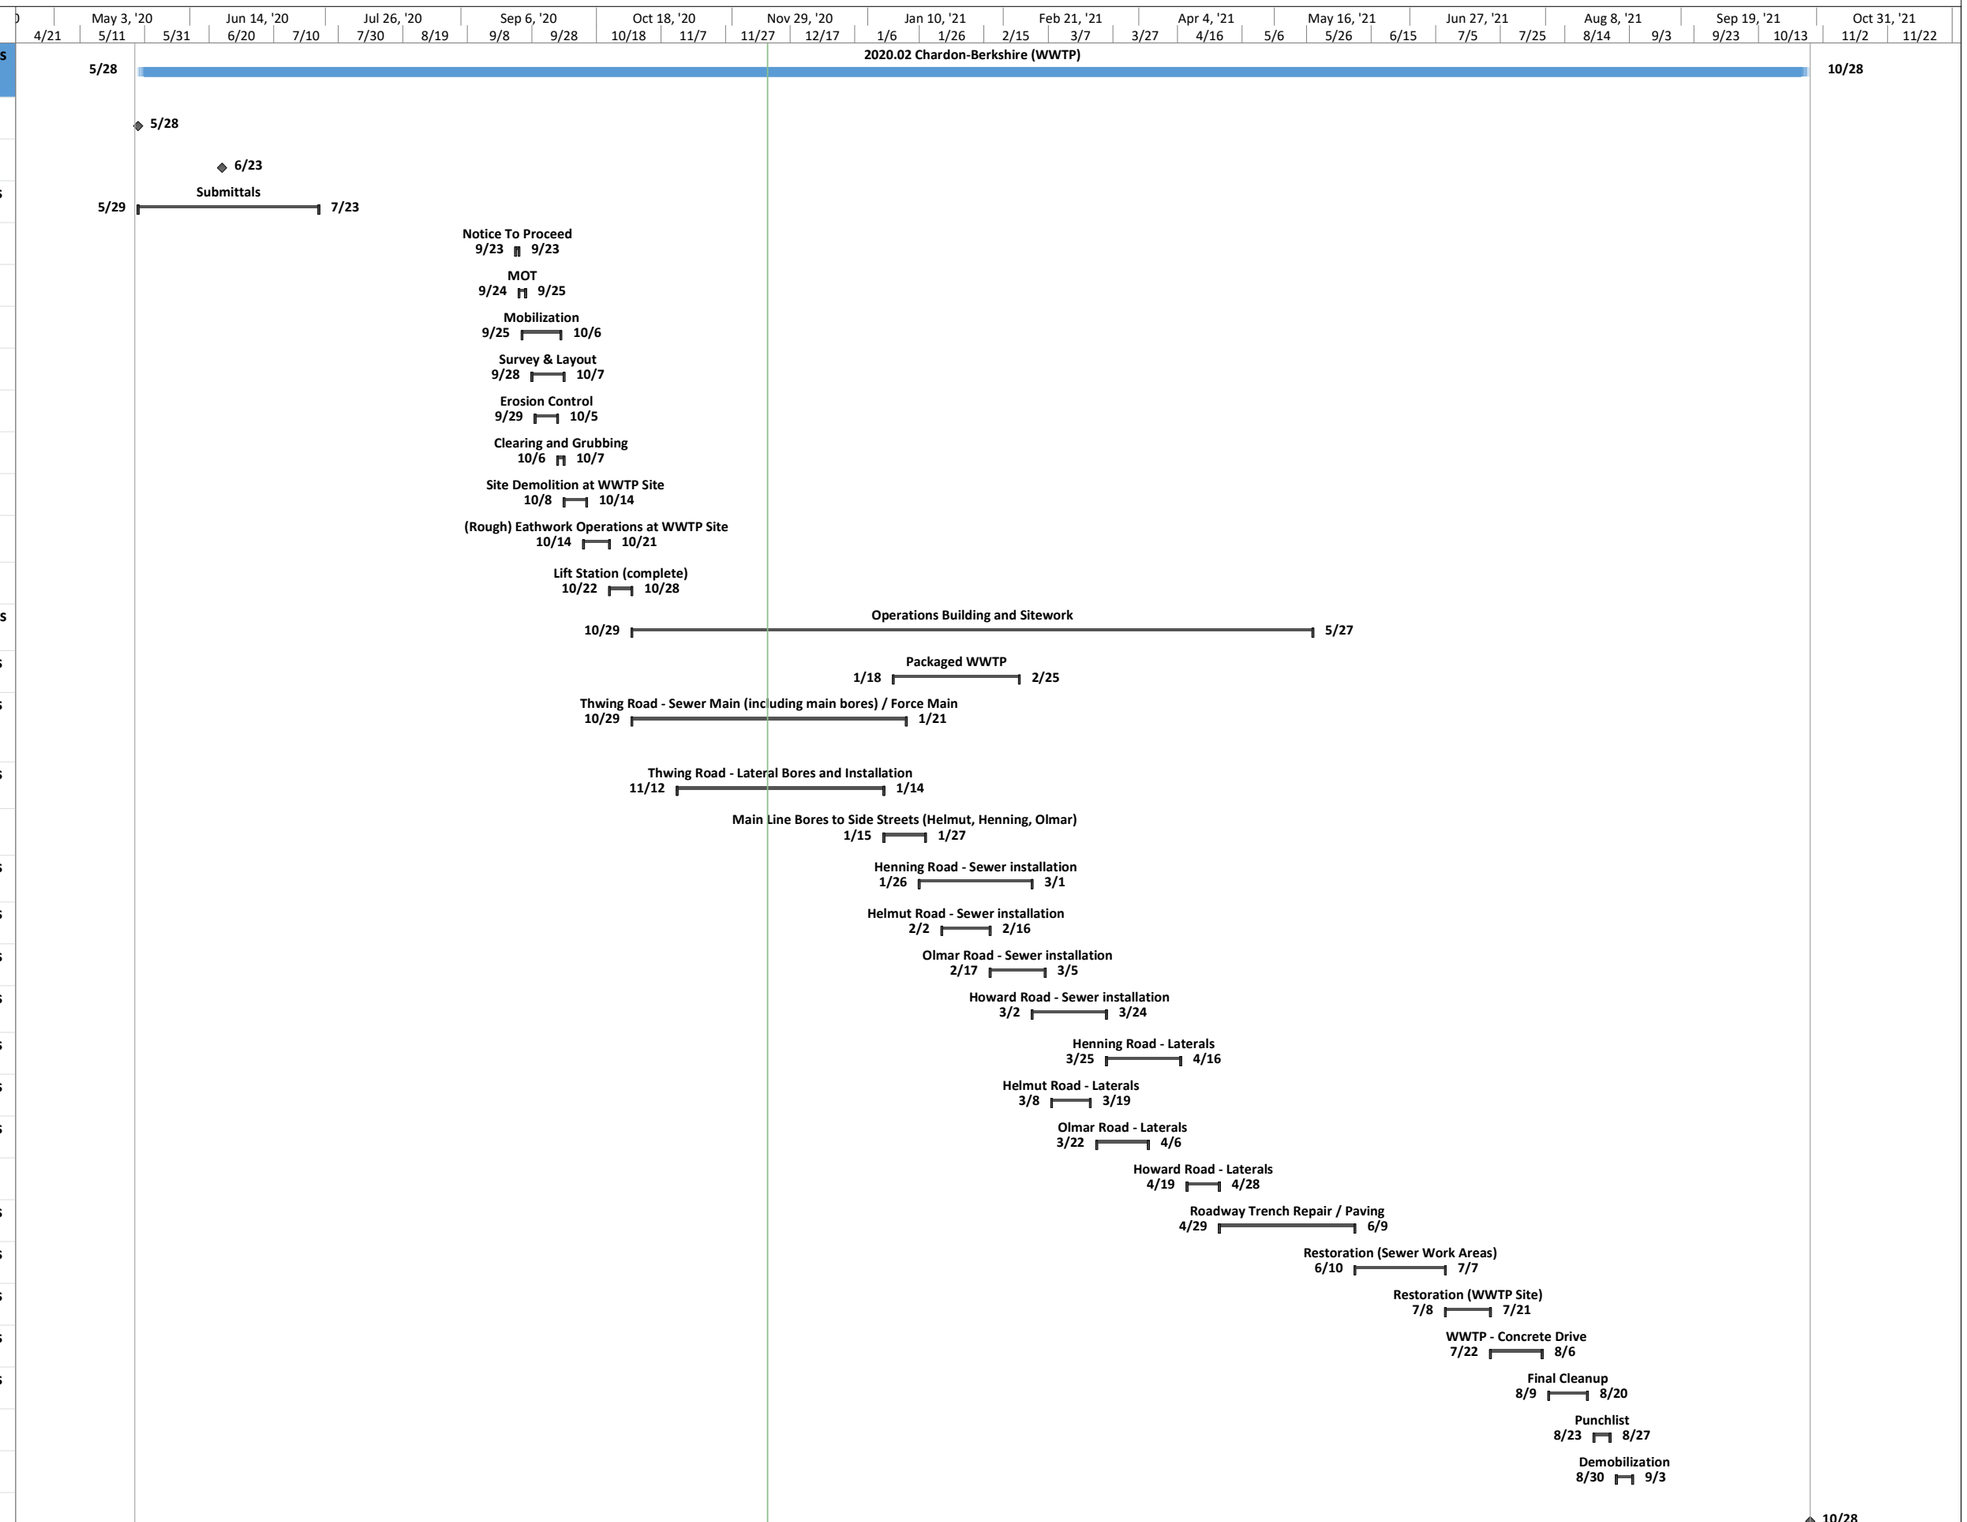
ID	Task Name	Start	Finish	Duration
1	**2020.02 Chardon-Berkshire (WWTP)**	**Thu 5/28/20**	**Thu 10/28/21**	**371 days**
2	Notice of Award	Thu 5/28/20	Thu 5/28/20	1 day
3	Executed Contract	Tue 6/23/20	Tue 6/23/20	1 day
4	**Submittals**	**Fri 5/29/20**	**Thu 7/23/20**	**40 days**
23	**Notice To Proceed**	**Wed 9/23/20**	**Wed 9/23/20**	**1 day**
25	**MOT**	**Thu 9/24/20**	**Fri 9/25/20**	**2 days**
28	**Mobilization**	**Fri 9/25/20**	**Tue 10/6/20**	**8 days**
30	**Survey & Layout**	**Mon 9/28/20**	**Wed 10/7/20**	**8 days**
33	**Erosion Control**	**Tue 9/29/20**	**Mon 10/5/20**	**5 days**
39	**Clearing and Grubbing**	**Tue 10/6/20**	**Wed 10/7/20**	**2 days**
42	**Site Demolition at WWTP Site**	**Thu 10/8/20**	**Wed 10/14/20**	**5 days**
48	**(Rough) Eathwork Operations at WWTP Site**	**Wed 10/14/20**	**Wed 10/21/20**	**6 days**
53	**Lift Station (complete)**	**Thu 10/22/20**	**Wed 10/28/20**	**5 days**
58	**Operations Building and Sitework**	**Thu 10/29/20**	**Thu 5/27/21**	**149 days**
72	**Packaged WWTP**	**Mon 1/18/21**	**Thu 2/25/21**	**29 days**
78	**Thwing Road - Sewer Main (including main bores) / Force Main**	**Thu 10/29/20**	**Thu 1/21/21**	**59 days**
89	**Thwing Road - Lateral Bores and Installation**	**Thu 11/12/20**	**Thu 1/14/21**	**44 days**
92	**Main Line Bores to Side Streets (Helmut, Henning,**	**Fri 1/15/21**	**Wed 1/27/21**	**9 days**
97	**Henning Road - Sewer installation**	**Tue 1/26/21**	**Mon 3/1/21**	**25 days**
100	**Helmut Road - Sewer installation**	**Tue 2/2/21**	**Tue 2/16/21**	**11 days**
103	**Olmar Road - Sewer installation**	**Wed 2/17/21**	**Fri 3/5/21**	**13 days**
106	**Howard Road - Sewer installation**	**Tue 3/2/21**	**Wed 3/24/21**	**17 days**
109	**Henning Road - Laterals**	**Thu 3/25/21**	**Fri 4/16/21**	**17 days**
112	**Helmut Road - Laterals**	**Mon 3/8/21**	**Fri 3/19/21**	**10 days**
115	**Olmar Road - Laterals**	**Mon 3/22/21**	**Tue 4/6/21**	**12 days**
118	**Howard Road - Laterals**	**Mon 4/19/21**	**Wed 4/28/21**	**8 days**
121	**Roadway Trench Repair / Paving**	**Thu 4/29/21**	**Wed 6/9/21**	**30 days**
124	**Restoration (Sewer Work Areas)**	**Thu 6/10/21**	**Wed 7/7/21**	**20 days**
127	**Restoration (WWTP Site)**	**Thu 7/8/21**	**Wed 7/21/21**	**10 days**
130	**WWTP - Concrete Drive**	**Thu 7/22/21**	**Fri 8/6/21**	**12 days**
133	**Final Cleanup**	**Mon 8/9/21**	**Fri 8/20/21**	**10 days**
136	**Punchlist**	**Mon 8/23/21**	**Fri 8/27/21**	**5 days**
139	**Demobilization**	**Mon 8/30/21**	**Fri 9/3/21**	**5 days**
142	Substantial Completion (400-day from NTP)	Thu 10/28/21	Thu 10/28/21	1 day
